



SARIA Project Updates

Project Updates

- Three SARIA Projects
 - Gartrell Bridge
 - Aurora Parkway Bridge
 - Gun Club Road Multi-modal Improvements




Gartrell Bridge Widening



Project Overview & Update

- Construct 5-lane roadway section over E-470
- Funding Partners
 - Bridge Design: Aurora, SARIA
 - Signal Design: Aurora
 - Temporary Signal Construction: E470
 - Construction: SARIA and E470
- Project was successfully bid
 - 11 bids received
 - Myers & Sons - winning bid
 - Estimated cost \$10.10M
 - Successful Bid \$8.84M
 - Potential cost savings \$1.26M

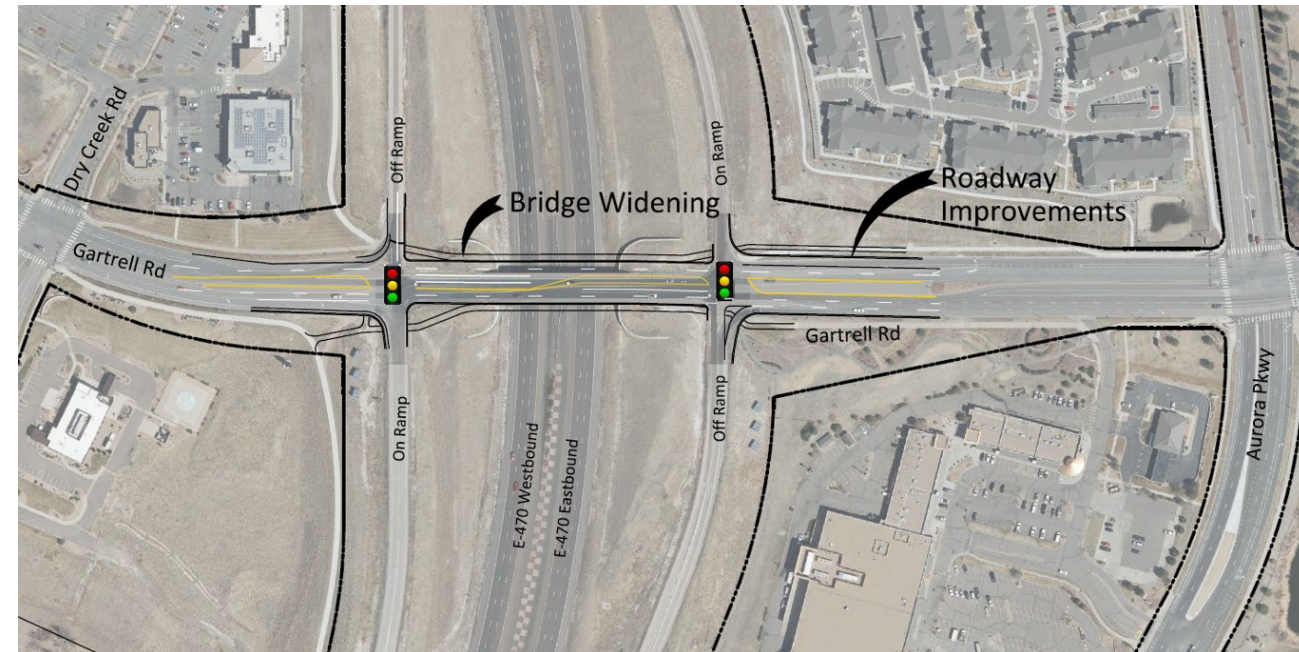

Gartrell Bridge Widening



Funding Overview

Gartrell Bridge Widening	
\$	Description
\$950,000	Original Design
\$500,000	SARIA share (previous IGA)
\$450,000	SARIA design reimbursement
\$250,000	E470 Construction Management Cost
\$10,100,000	Estimated Construction Cost
\$10,800,000	Executed SARIA IGA

Status Update

- Construction anticipated to begin spring 2026 and last 12 months




Aurora Parkway Bridge



Project Overview

- Design and construct bridge over E-470 for future Aurora Parkway extension to Parker Road
- Funding Partners
 - Bridge: Aurora, SARIA
 - Roadway: adjacent developers
- Timeline
 - Final Design – TBD – developer driven
 - Construction – TBD – developer driven

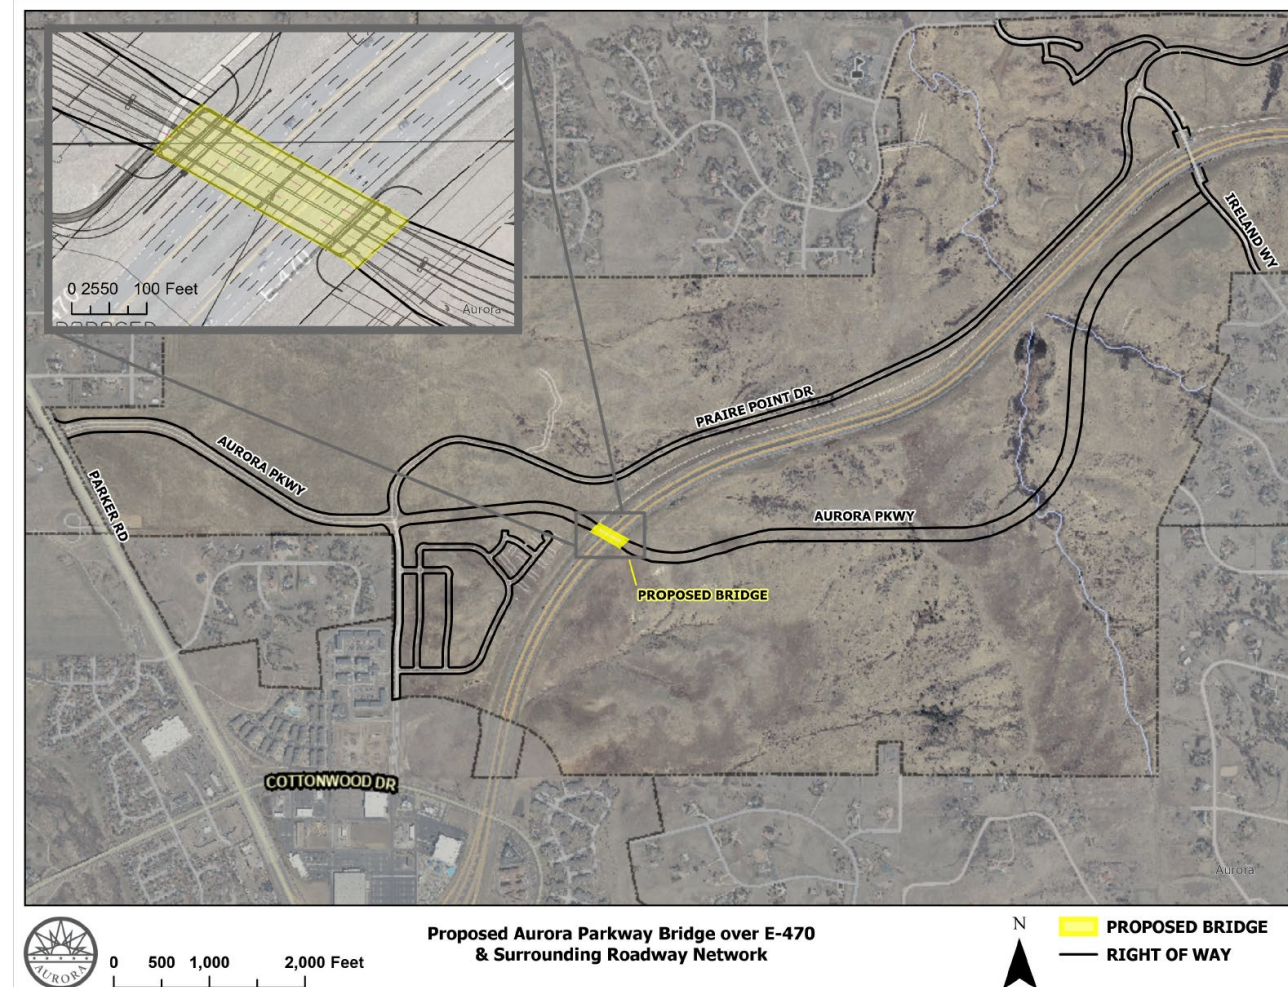

Aurora Parkway Bridge



Funding Update

Aurora Parkway Bridge	
\$	Description
\$700,000	Original Design (30% full bridge, 100% interim bridge)
\$333,000	Remaining Design Funds
\$390,000	Additional Design Funds Needed for Full Bridge Final Design
\$800,000	Additional Funds Needed for CORE Construction
\$250,000	E470 Construction Management Cost
\$10,076,000	Construction - Interim Bridge
\$14,966,000	Final Design and Construction - Full Bridge
\$4,000,000	COA Impact Fee (maximum contribution)
\$11,516,000	Executed SARIA IGA

Status Update


- 60% plans complete
- Anticipate 18 months to complete final design in coordination with developers and trail designs
- Public Works staff continues to attend developer coordination meetings

Gun Club Multimodal Improvements



Project Overview

- Design 4-lane roadway section (expandable to future 6-lane section) from Quincy Avenue to Aurora Parkway
- Funding Partners
 - Preliminary Design: SARIA, Arapahoe County
 - Final Design: Federal grant, Aurora, Arapahoe County
- Timeline
 - Preliminary Design – complete
 - Final Design - 2025-27
 - Construction - TBD

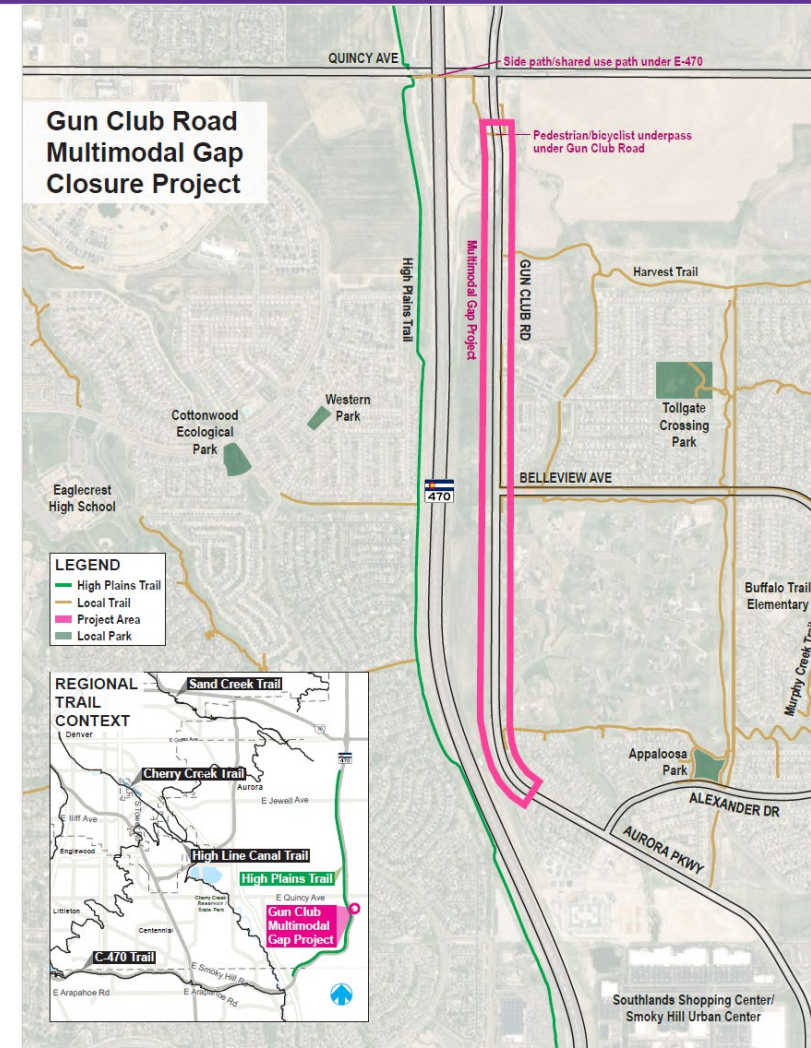

Gun Club Multimodal Improvements



Funding Update

Gun Club Multimodal Improvements	
\$	Description
\$4,600,000	Preliminary Design and Utility Relocation
\$2,500,000	Final Design
\$33,000,000	Estimated Construction Cost
\$1,700,000	Executed SARIA IGA

Status Update

- Preliminary design complete
- Transmission line relocation ongoing
- Coordination with Arapahoe County and adjacent developer ongoing
- Ongoing final design
- The project is included in the Build Up Aurora proposed project list. Visit [Build Up Aurora](#) | [Engage Aurora](#) for more information.





Thank you
